




Fiber Tracker Schedule


- Fiber Tracker Mechanical Assembly
 - ◆ Critical path is ribbon mounting
 - Can mount 4/day with extended shifts (270 to do, C1,2,4,5,6,7,8)
 - Looking into alternate adhesive - 6/day (ribbon fab can keep up)
 - Adds contingency to schedule

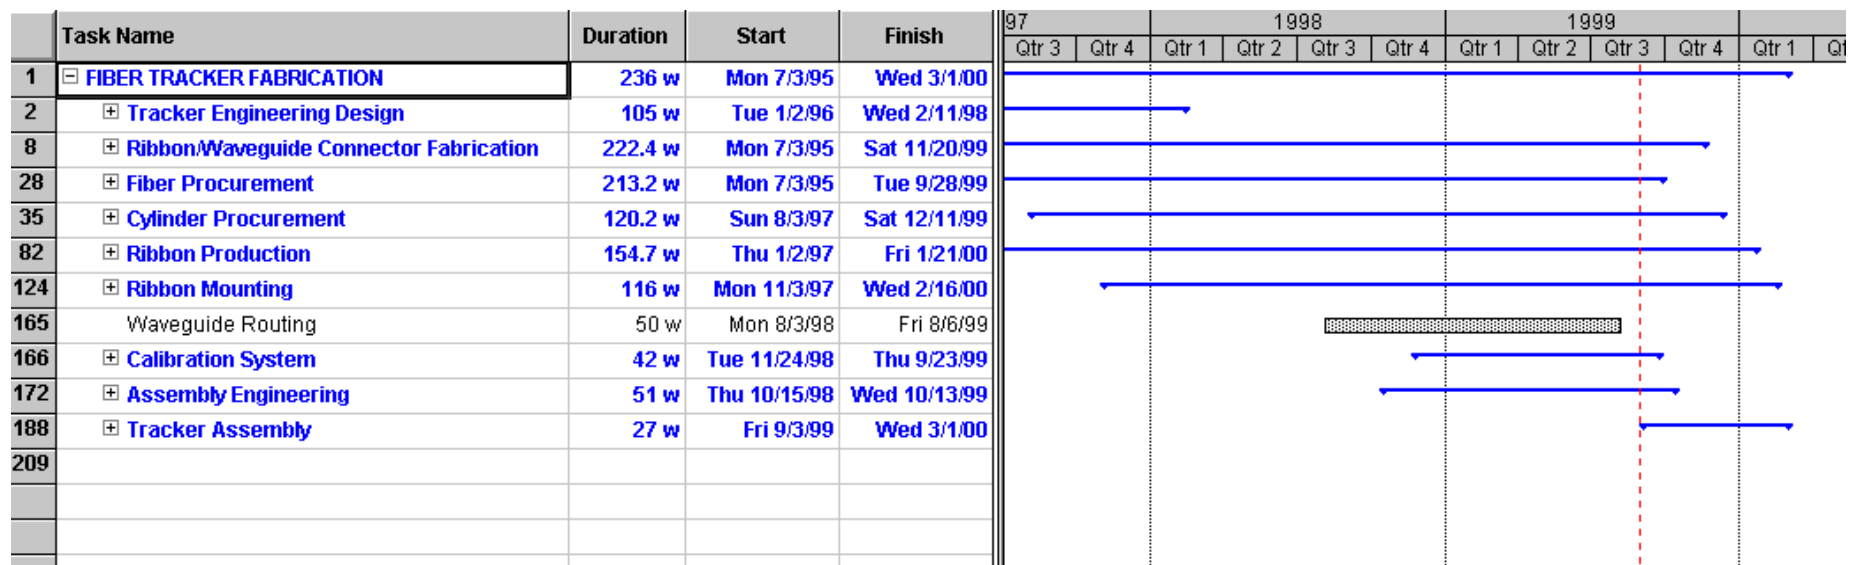




Fiber Tracker Schedule

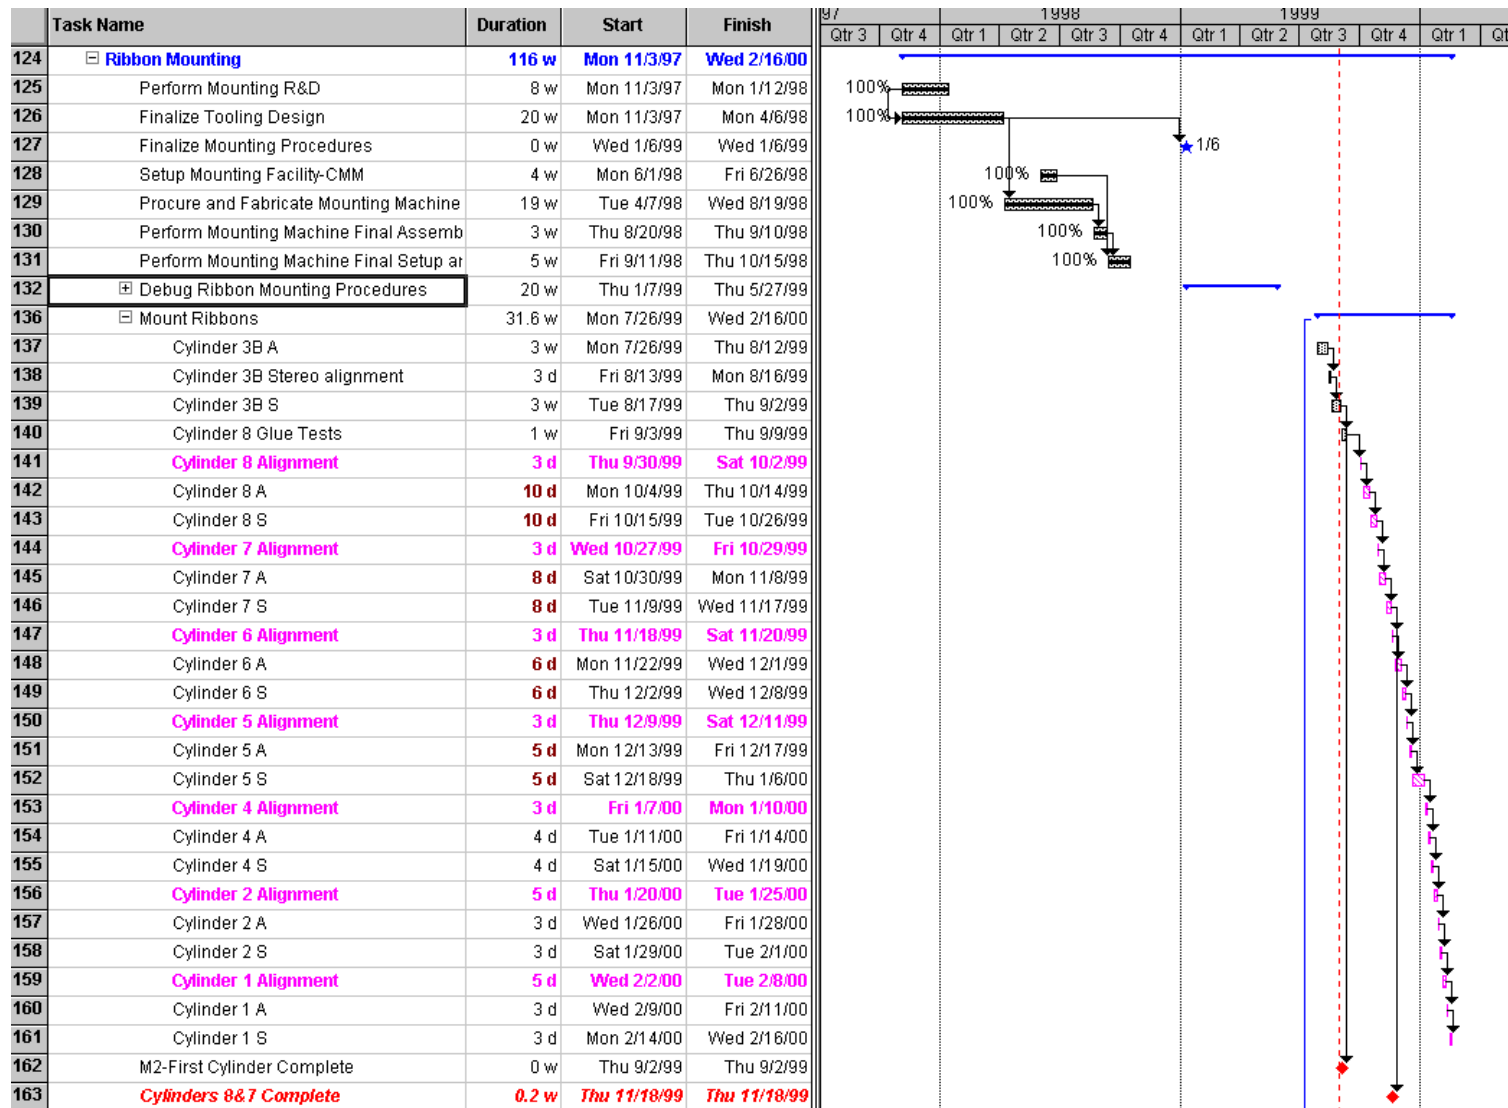




Fiber Tracker Schedule

- VLPC Cassettes

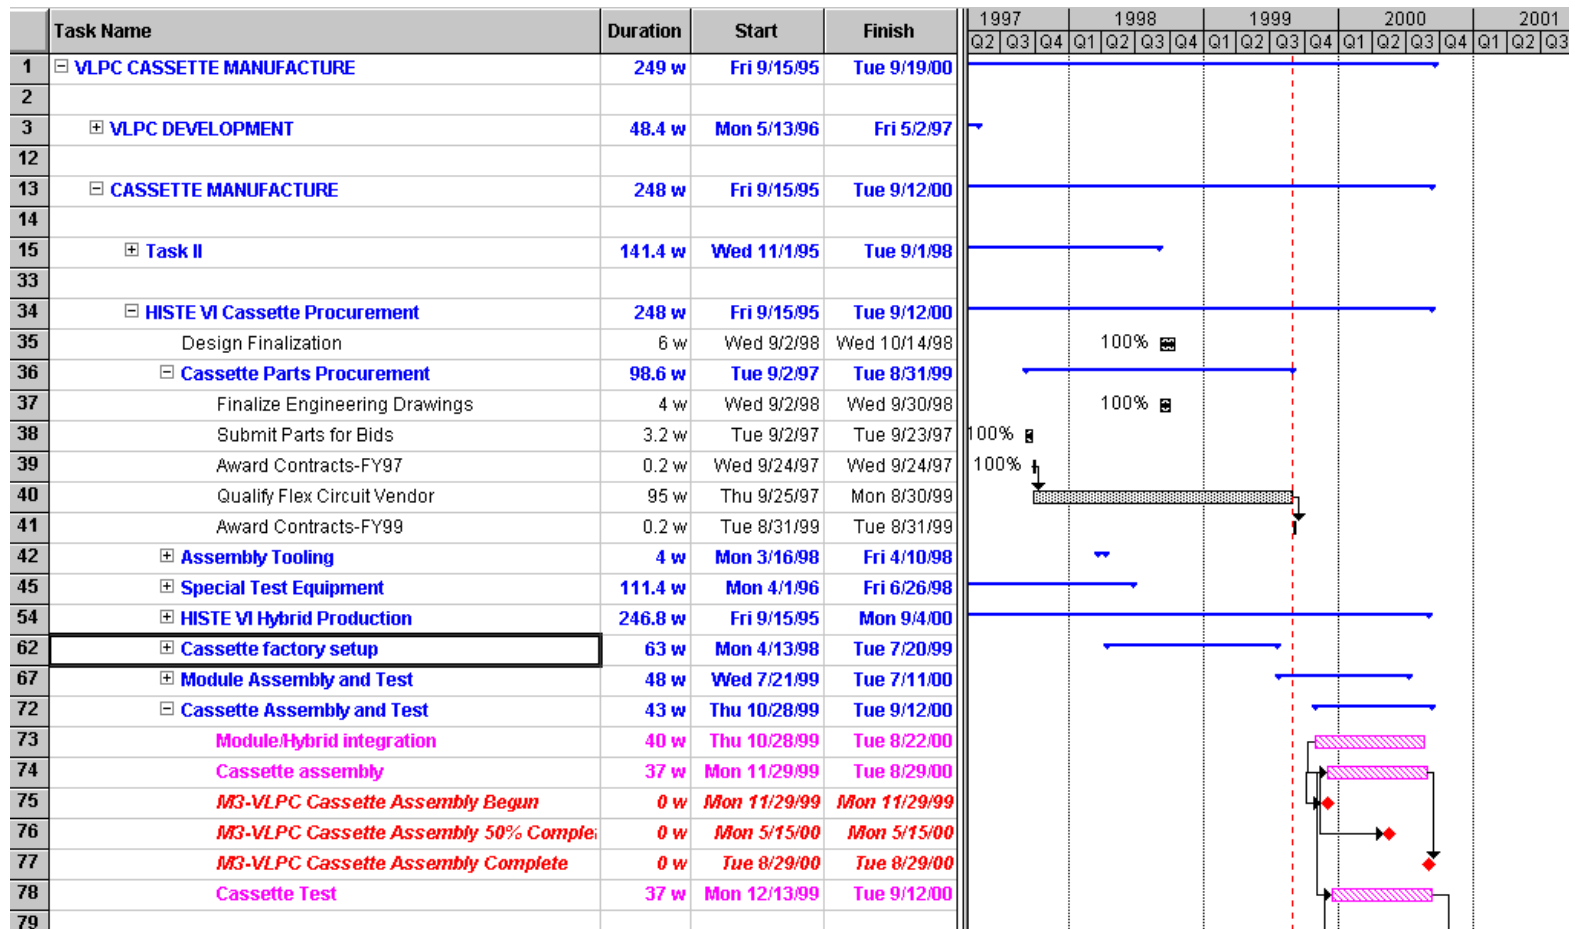



Fiber Tracker Schedule

- Waveguides

	Task Name	Duration	Start	Finish	98	1999				2000			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
1	Waveguide Production	207.2 w	Mon 4/1/96	Fri 5/5/00									
2	Design and Setup Factory	30 w	Mon 4/1/96	Wed 10/30/96									
3	Notre Dame MOU FY98	0.2 w	Mon 8/3/98	Mon 8/3/98									
4	Perform Design R&D	16 w	Tue 9/15/98	Wed 1/20/99									
5	Perform Pre-production Checkout	28 w	Thu 1/21/99	Fri 8/6/99									
6	Waveguide Facility Ready	0 w	Fri 8/6/99	Fri 8/6/99									
7	Indiana Univ MOU FY99	0.2 w	Wed 3/3/99	Wed 3/3/99									
8	Produce Waveguides	41 w	Sat 8/7/99	Fri 5/5/00									
9	Spool and Sheath Fiber	40 w	Sat 8/7/99	Fri 4/28/00									
10	Connectorize curved end	40 w	Fri 8/13/99	Fri 5/5/00									
11	Connectorize/map 128 X 2 End	40 w	Fri 8/13/99	Fri 5/5/00									
12	Perform Final Test	40 w	Fri 8/13/99	Fri 5/5/00									
13													
14	Fabricate Clear Fiber Bundles	8 w	Mon 3/13/00	Fri 5/5/00									
15	M3-Fiber Tracker Waveguide Production Begun	0 w	Sat 8/7/99	Sat 8/7/99									
16	Waveguide Production 50% Complete	0 w	Sat 1/15/00	Sat 1/15/00									

