

L1_Cal Test stand Operations Mode pORC review response.


Dan Wolff and Walt Jaskierny reviewed the L1_Cal sidewalk test stand in the Operations mode configuration on December 13, 2005. All documentation regarding the system can be found at the following link:

<http://d0server1.fnal.gov/users/bagby/www/L1defaultorc.htm>

The following responses to the pORC inspection are submitted for your review.

1. Install a protective covering over the Control crate backplane.

Response: A right angle Lexan cover, as shown below, has been secured over the backplane power bus area on the Control crate backplane.

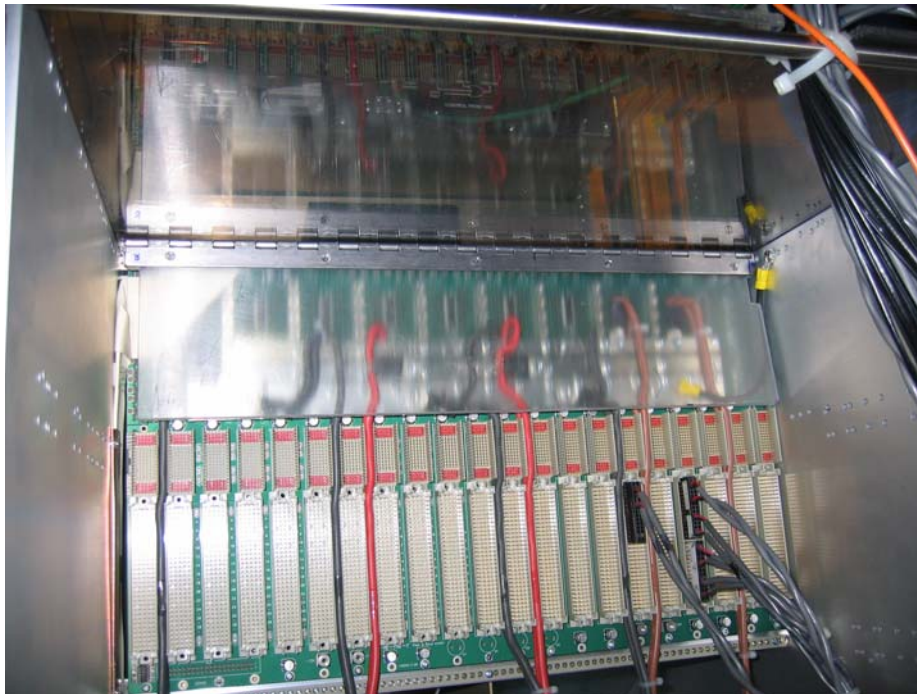

2. Verify that the Rack Monitor Interface (RMI) has been tested.

Response: The RG58 trip cables from the Rack Monitor Interface (RMI) to the fault boxes have been connected. Spray smoke has been used to verify the ADF crate power supplies in rack S109/S111 are disabled when smoke is present in the rack
